


STATE/LOCAL PARTNERSHIP PROGRAM (SLPP) PROJECT
PLEASANT VALLEY ROAD (SR49)/PATTERSON DRIVE
SIGNALIZATION



Project Description

The Pleasant Valley Road (State Route 49)/Patterson Drive Signalization project is located in Diamond Springs and signalized the intersection of Pleasant Valley Road (also known as State Route 49 in this location) with Patterson Drive. The project significantly improved safety and provided much needed congestion relief. Project improvements included:

- Intersection signalization
- Left- and right-turn lanes
- New bicycle and pedestrian facilities to Pleasant Valley Road / State Route 49

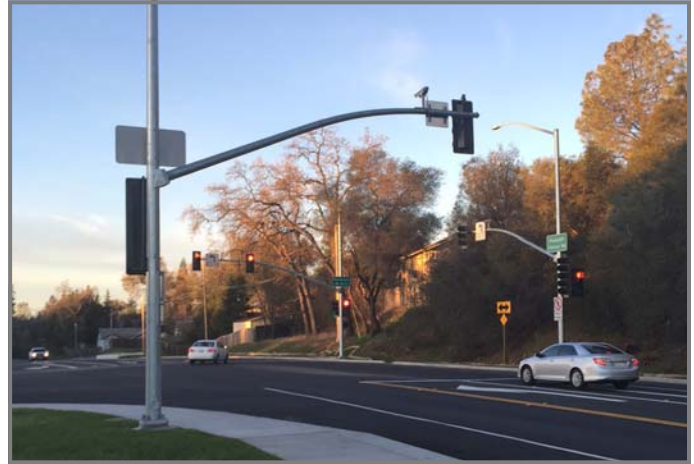

Current Project Status

SLPP funding was programmed to the project at the October 26/27, 2011 CTC meeting. The funding originally needed to be allocated by the June 27-28, 2012 CTC meeting, but the County requested and received a 12-month allocation extension at the August 22, 2012 CTC meeting. On November 5, 2013, the Board of Supervisors awarded the construction contract to Western Engineering Contractors, Inc. for \$1,747,742.02. Full construction began in spring 2014 and was completed in fall 2014.

Upcoming Activities

- None. This project is complete.

PROJECT FUNDING DETAIL				
Project Phase	Amount Programmed	Source	Status	Project Cost
PA&ED	\$372,000	Uniform Developer Fee (TIM)	Complete	\$372,000
PS&E	\$626,000	Uniform Developer Fee (TIM)	Complete	\$626,000
ROW	\$700,000	Uniform Developer Fee (TIM)	Complete	\$700,000
Construction	\$600,000	Uniform Developer Fee (TIM)	Programmed	\$600,000
	\$600,000	SLPP	Allocated	\$600,000
	\$1,000,000	SHOPP	Programmed	\$1,000,000
TOTAL	\$3,898,000			\$3,898,000
